

COVID-19 Testing Site, Accrington

PROJECT BACKGROUND & REQUIREMENT:

As part of the Government's push to improve local COVID-19 testing access, a temporary facility was fast-tracked at Eastgate Car Park.

Fully DDA-compliant ramps and steps to the building were urgently required to be installed ahead of the site's end-of-week launch.

Unlike traditional poured concrete or fixed timber solutions, which are single-use and labour-intensive to construct, our modular access systems offered quick and easy assembly, straightforward removal, and full reusability—providing the flexibility and efficiency required for temporary projects such as this.

DESIGN PHASE:

Within 24 hours of receiving the initial enquiry and site dimensions, we delivered full 2D and 3D technical drawings along with a detailed quotation for the contractor.

APPLICATION

Healthcare

LOCATION


Accrington, Hyndburn

SYSTEM


Modular Ramp & Steps

SERVICE PACKAGE

Ramp Rental

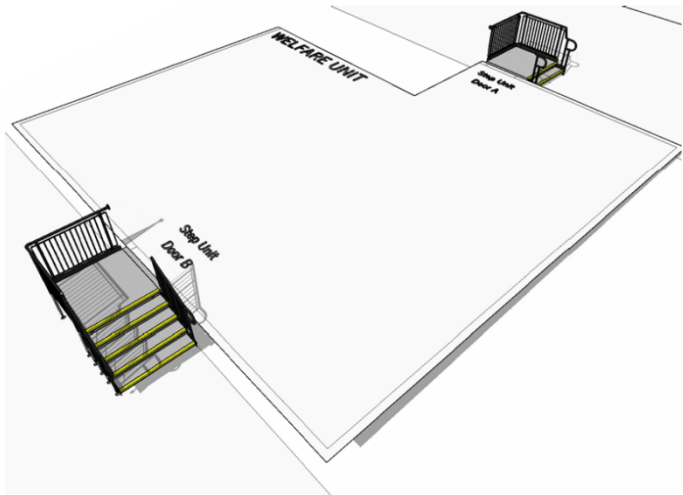

MAIN UNIT

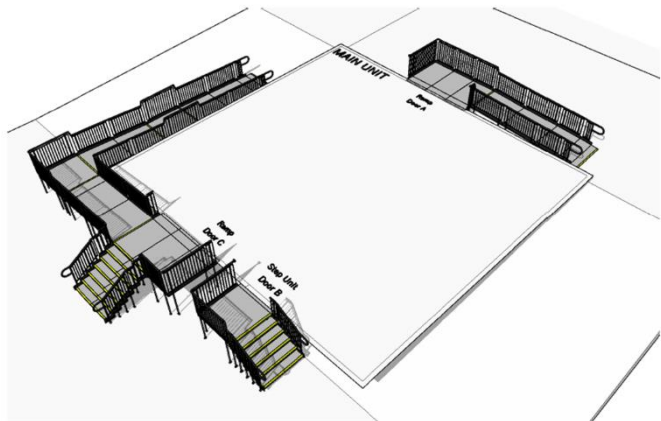

INSTALLATION:

Measurements were received on Monday evening. By Tuesday morning, all components had been picked, packed, and dispatched—arriving on site first thing Wednesday.

Installation also began that Wednesday by our fitting team, with the system fully operational and ready for use by Thursday at midday.


We lived up to our name—delivering the entire project in under a week. This was made possible by our fully in-house team, including estimators, designers, a site surveyor, and skilled installers, all working in sync to meet the tight deadline.

With all components available from stock, we were ready to move the moment the green light was given.

FEATURES INCLUDED:

- Looped Trombone Ends – Prevent clothing from snagging at handrail ends.
- Slip-resistant Mesh Platform - A multi-directional, self-draining walkway made from galvanised steel mesh.
- Anti-climbing Infill Handrail - Prevents climbing and reduces the risk of falls through open sections.
- Continuous Handrail - Offers uninterrupted support along the walkway.
- Standard Colour: Black - A powder-coated finish provides increased durability over conventional paint.
- Adjustable Telescopic Legs - Accommodate varying threshold heights with ease.
- Slip-Resistant Yellow Stair Nosings - Improve visibility of edges and level changes, especially for visually impaired users.
- Rest Platform – A rest platform at 5 metres to provide users with a place to pause.
- 1100mm High Rail – These Handrails installed on all level sections for safety and support.
- Continuous Handrail- A continuous handrail system that ensures users have uninterrupted support throughout the ramp.



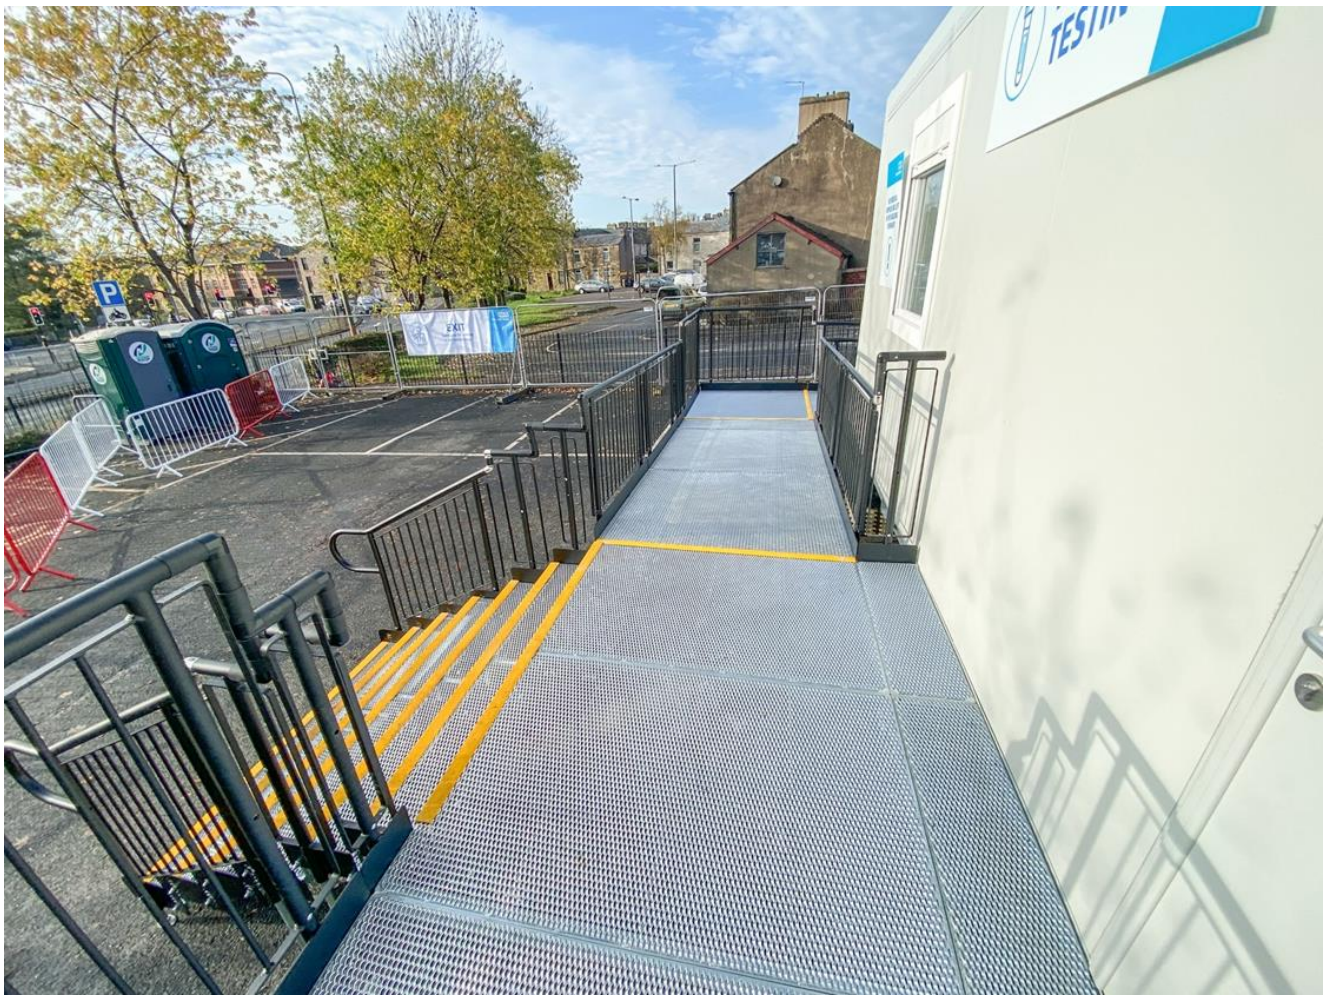

EMAIL: sales@rapidramp.co.uk
VISIT: rapidramp.co.uk

HOURS: Open 8am - 5pm, Monday to Friday
ADDRESS: Riverside Works, Church Ln, Etchingam, TN19 7AS

Do you require modular
ramps and steps?

Request a quick price
